CYPRESS BRIDGE REPLACEMENT SCHEDULE
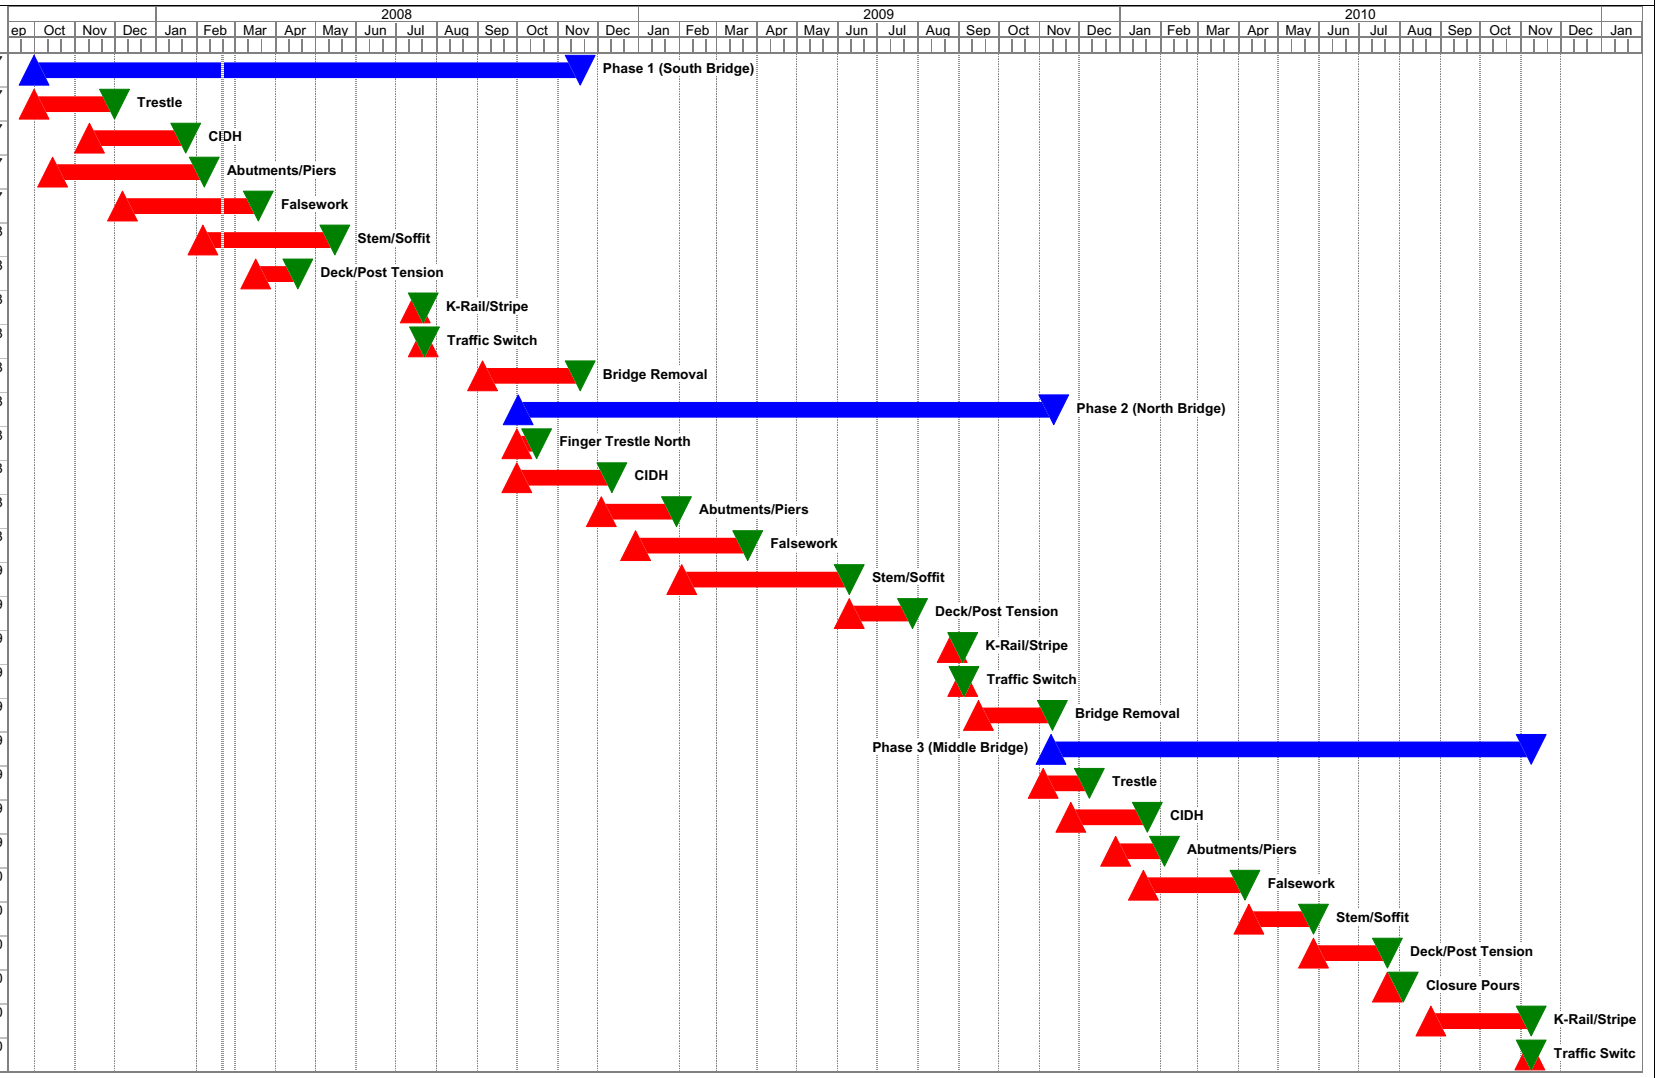
ID	Task Name	Start
1	**Phase 1 (South Bridge)**	Mon 10/01/07
2	Trestle	Mon 10/01/07
3	CIDH	Mon 11/12/07
4	Abutments/Piers	Mon 10/15/07
5	Falsework	Fri 12/07/07
6	Stem/Soffit	Wed 02/06/08
7	Deck/Post Tension	Mon 03/17/08
8	K-Rail/Stripe	Wed 07/16/08
9	Traffic Switch	Tue 07/22/08
10	Bridge Removal	Fri 09/05/08
11	**Phase 2 (North Bridge)**	Thu 10/02/08
12	Finger Trestle North	Wed 10/01/08
13	CIDH	Wed 10/01/08
14	Abutments/Piers	Thu 12/04/08
15	Falsework	Tue 12/30/08
16	Stem/Soffit	Tue 02/03/09
17	Deck/Post Tension	Wed 06/10/09
18	K-Rail/Stripe	Thu 08/27/09
19	Traffic Switch	Fri 09/04/09
20	Bridge Removal	Wed 09/16/09
21	**Phase 3 (Middle Bridge)**	Tue 11/10/09
22	Trestle	Wed 11/04/09
23	CIDH	Wed 11/25/09
24	Abutments/Piers	Tue 12/29/09
25	Falsework	Tue 01/19/10
26	Stem/Soffit	Fri 04/09/10
27	Deck/Post Tension	Fri 05/28/10
28	Closure Pours	Fri 07/23/10
29	K-Rail/Stripe	Wed 08/25/10
30	Traffic Switch	Mon 11/08/10
